Protrak Construction Management

User Guide for
Protrak Project Management Module

Submitted to

MOUNT MERU GROUP

Submitted by

PRORIGO SOFTWARE PRIVATE LIMITED

601, OneWest, Balewadi High Street,
Baner, Pune, Maharashtra, India - 411045
www.prorigo.com | www.protrak.ai

PROPRIETARY RIGHTS NOTICE: This document contains data considered Proprietary and Confidential by PRORIGO Software Pvt. Ltd. No part of this material may be reproduced or transmitted in any form or by any means, electronic, mechanical, or otherwise, including photocopying and recording or in connection with any information storage or retrieval system, without the permission in writing from PRORIGO Software Pvt. Ltd.

1 Introduction

This user guide is designed to help project managers, planning engineers, and site engineers efficiently set up, plan, schedule, and track projects using Protrak. The module provides a structured approach to project management, enabling seamless collaboration, real-time progress tracking, and automated scheduling to optimize project timelines.

2 Login

2.1 Login Credential

When the Admin creates a user, following email will be sent to users email id to help them with login. The user has to click on "Click Here" to get started

protrak.support@prorigosoftware.com

Date: 15-03-2025 14:13:58

Subject: Your Protrak Account Created Successfully.

Hi sexahib,
Welcome! Your Protrak account is created successfully.

You can log in by using the following credentials:
User Name: sexahib232@erapk.com
Password: $FIvE)iF

Following are the steps to change the password:
Settings > Personal > Change Password.
Click Here to get started.

You can also download Protrak mobile app:

- For Android: Download from Google Play
- For iOS: Download from the App Store

This is a system-generated mail, please do not reply

Thank You.

Copyright © All rights reserved

2.2 Login and reset Password

2.2.1 Web: Login using the email and change the password (optional)

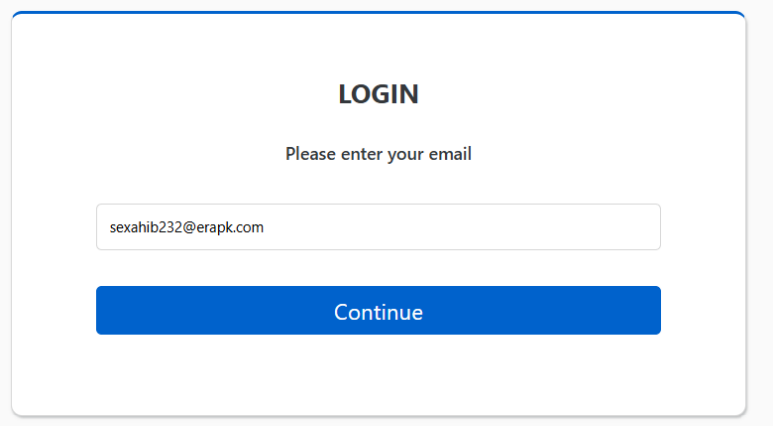



2.2.2 Mobile: Login using the email and change the password (optional)





Copyright © All rights reserved

3 Setting up Projects

- Users: Project Managers & Planning Engineers
- Log in to Protrak with your credentials

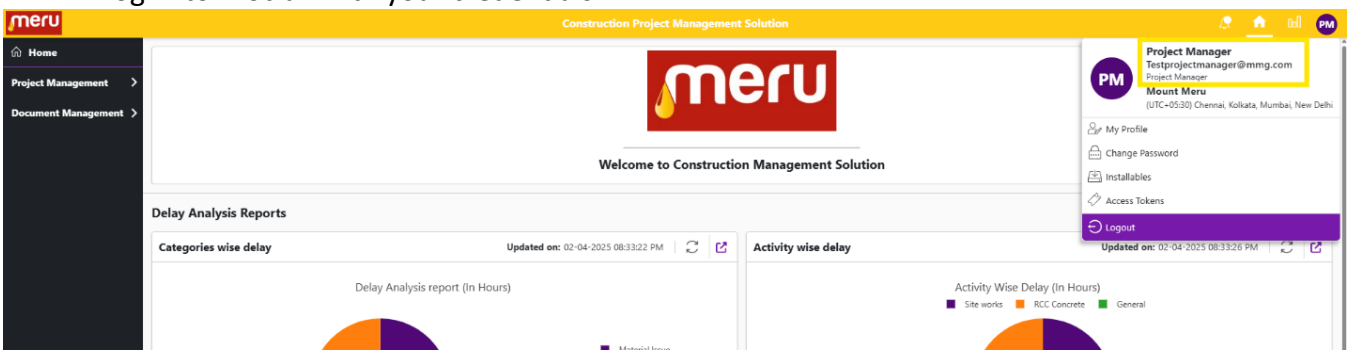

3.1 Creating a Project

1. Navigate to the 'Projects' tab and click on + Project'.



2. Enter the required project details: *Project Name, Project ID (auto-generated based on Country, SBU Code, and Year), Address of Project, Country, SBU Code, Year, Geo-location, Project Budget* and click 'Save'

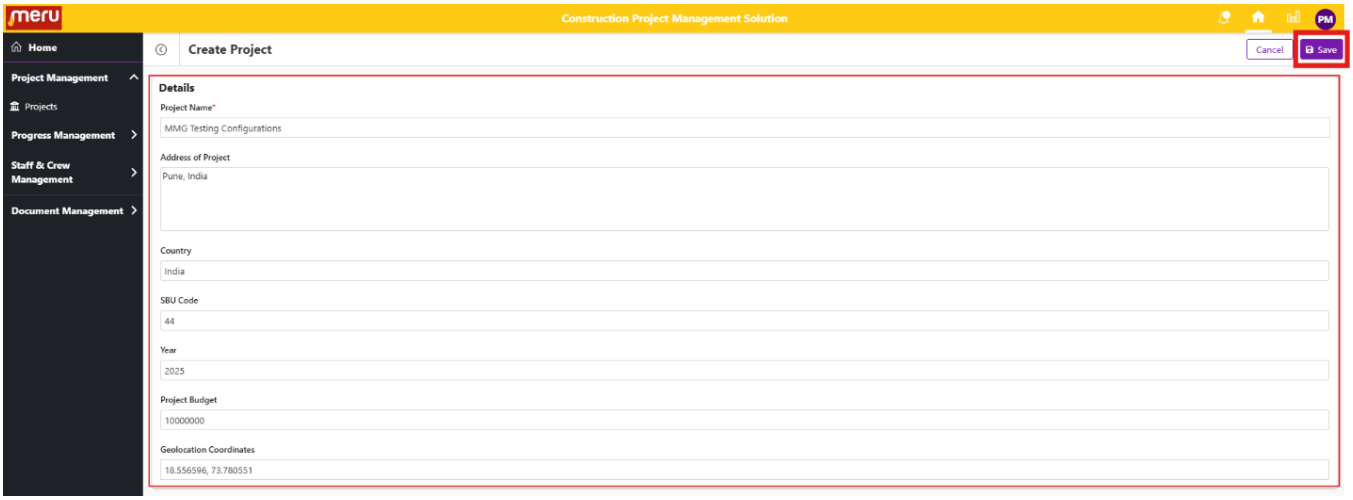

Copyright © All rights reserved

3. The 'Team' tab is now enabled, select the project team members by assigning roles and click 'Save'.

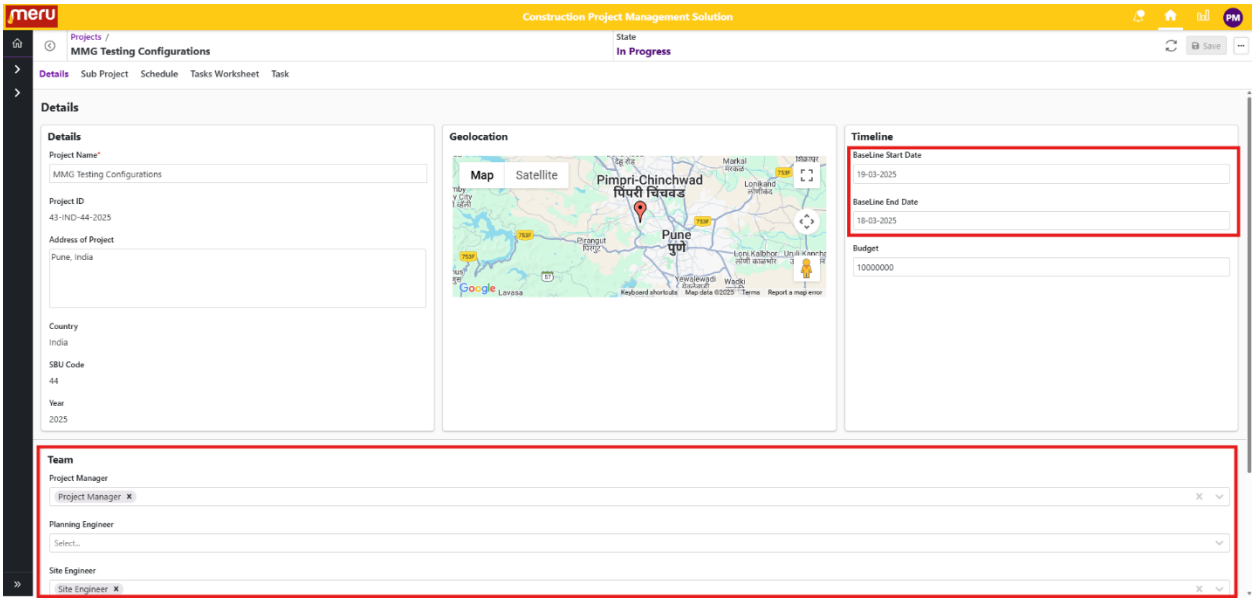

3.2 Adding Sub-Projects

1. Open the Project and navigate to the 'Sub-Project' tab and click on 'Add Sub-Project' tab.



2. Enter the required Sub-Project details: Sub-Project Name, Sub-Project Type (Picklist: RCC, Structural, PEB, Other), Total Square ft. of Sub-Project and click 'Done'.

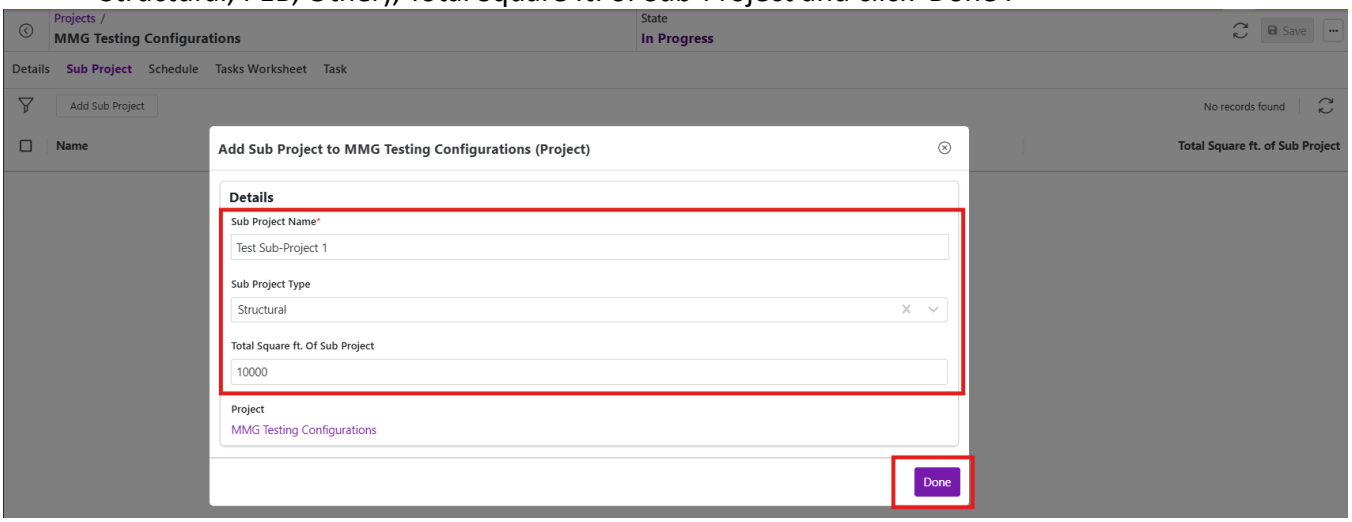

Copyright © All rights reserved

4 Planning & Scheduling Tasks

4.1 Importing Tasks

1. Navigate to the ‘Schedule’ tab in the Project and use the 'Import' functionality to import the MPP file project plan.



OR

2. Navigate to the 'Tasks Worksheet' tab to copy and paste the plan from an Excel file. Once it’s loaded, hit refresh and verify the imported tasks in the 'Schedule' tab.

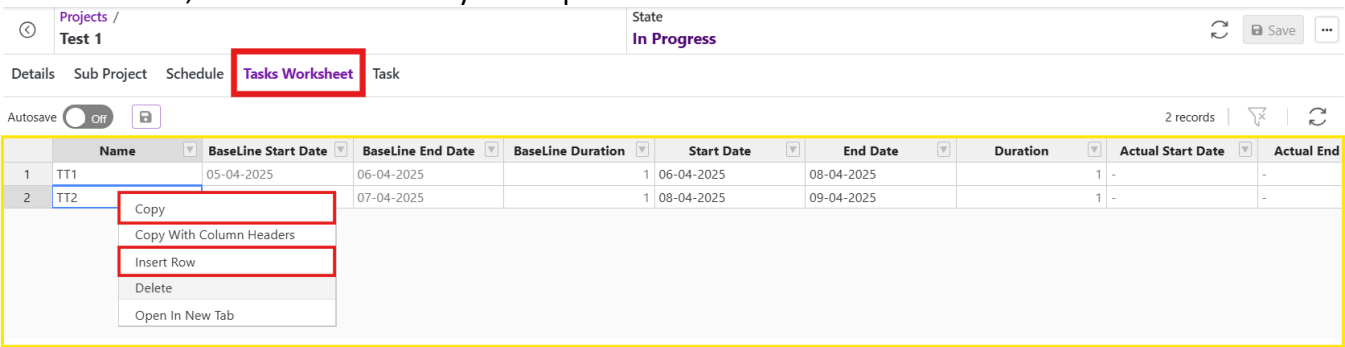

Note:

This might take up to 10 minutes to reflect as there are a lot of data being processed in the background. Click refresh to see the progress & the Gantt chart will be loaded completely once done.

4.2 Defining Task Hierarchies & Dependencies

1. Navigate to the 'Schedule' tab and use Indentation to define tasks, sub-tasks, and dependencies.

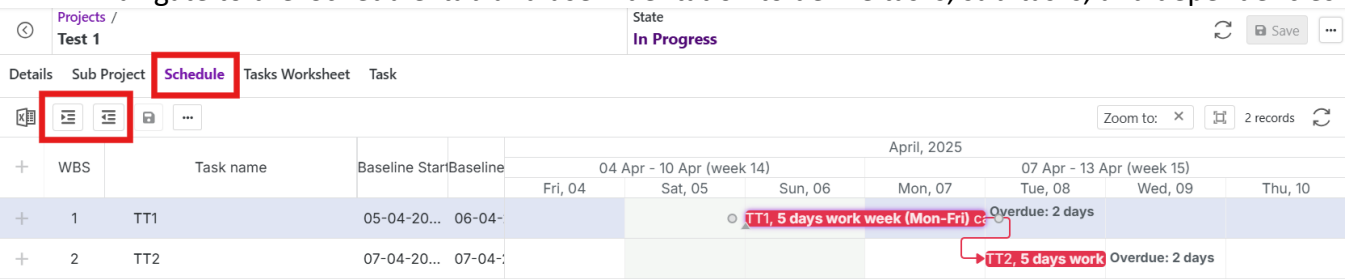

2. Key attributes for task planning:
   - Baseline Start & End Dates (approved by top management, non-editable)
   - Actual Start & End Dates (auto updated as tasks progress)
   - Duration (number of days required for task completion)
   - Predecessors (to link dependent tasks, e.g., Task B starts only after Task A is completed)
   - Assigned To (assign users to specific tasks)
   - Progress (auto updated based on checklists and work completed on-site)

Copyright © All rights reserved

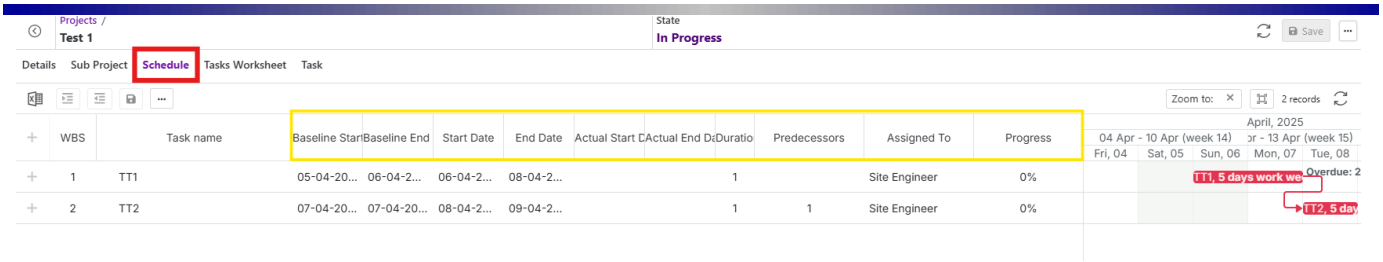

4.3 Updating Baseline

1. Once the schedule is created either from the schedule tab or Task Worksheet tab or using the import functionality, Project manager or Planning engineer can now adjust the tasks using the indentation tabs, adding duration to each task & setting predecessor to each task to ensure a task has some dependencies.

2. Now Project manager or Planning engineer can update the baseline of the project using the tab 'Update Baseline' on the top right corner, which will auto calculate based on all the conditions applied earlier to the schedule & auto populate the Baseline start date & Baseline End date for each task.

4.4 Automated Task Scheduling

- **Automated Task Scheduling** optimizes project timelines by dynamically adjusting dependencies and durations as updates are received from the site team.

5 Tracking Tasks & Work Progress

- User: Site Engineers
- Log in to Protrak with your credentials

5.1 Site Engineer Access and Permissions

Site Engineer Access and Permissions
Platform Access: Web and Mobile

- Site Engineers can access the platform via both web and mobile.
- Access is restricted to only the projects assigned to them.
- They can view only the tabs relevant to their role.

Project Tab Access: Under each assigned project, Site Engineers can view:

- Project Details: General information about the project.
- Sub-Projects: Details and breakdown of sub-projects.
- Schedule View Only: Access to the project schedule without edit permissions.

Copyright © All rights reserved

Schedule View Only Tab:

Web Access:

- Displays the project schedule in a Gantt Chart view.
- Strictly view-only, with no editing capabilities.

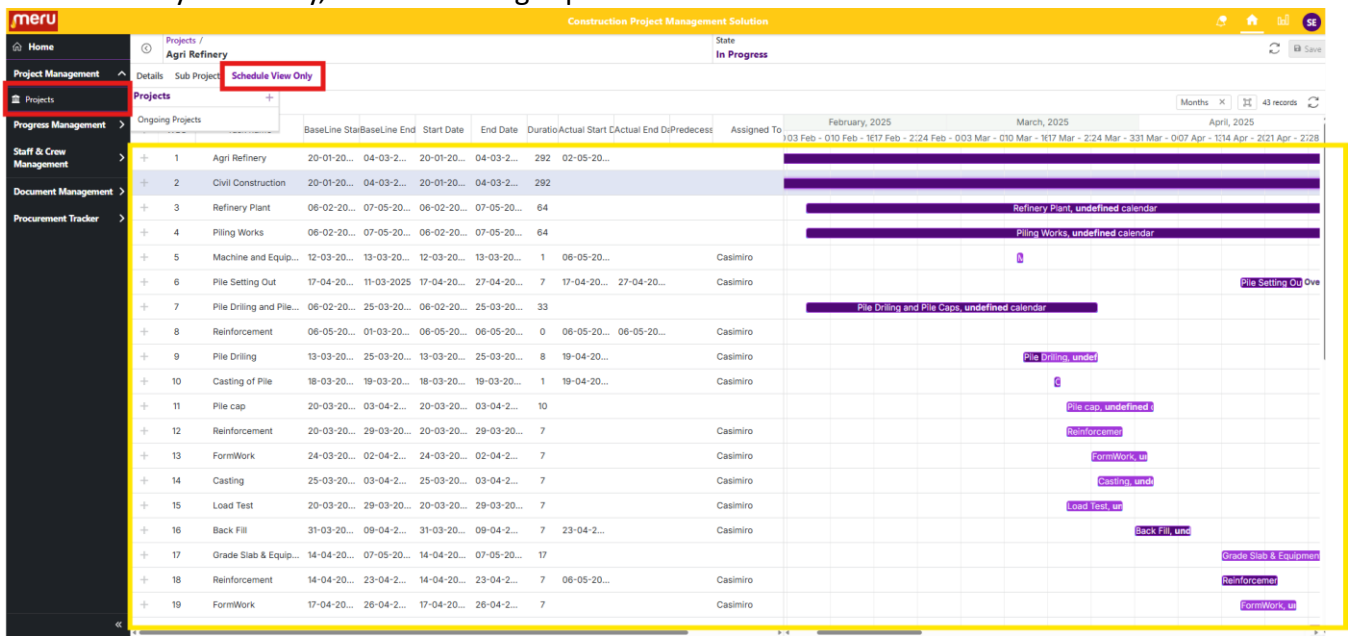

Mobile Access:

- Displays all tasks in a list format under the Schedule View Only tab.
- Similar to the web version, it is strictly for viewing.

5.2 Viewing & Managing Tasks

Managing tasks efficiently on the go is essential for site engineers. Protrak offers a streamlined task management interface, allowing user to view and manage tasks assigned to them through various dashboards. These dashboards enable the user to monitor progress, stay updated on ongoing and completed tasks, and promptly address any delays. This section will guide through navigating the task section on the mobile app, viewing tasks in different categories, and updating work progress.

1. Navigate to the 'Task' section.
2. Users can view tasks assigned to them in different dashboards:
   - All Tasks – Displays all assigned tasks.
   - Actionable Tasks – Highlights assigned tasks that are not yet completed.
   - Today's Tasks – Displays tasks due today.
   - Active Tasks – Lists ongoing tasks.
   - Completed Tasks – Shows completed tasks.
   - Delayed Tasks – Highlights tasks past their due date but not yet completed.

Copyright © All rights reserved

3. Click on a specific task to initiate it and update work progress.

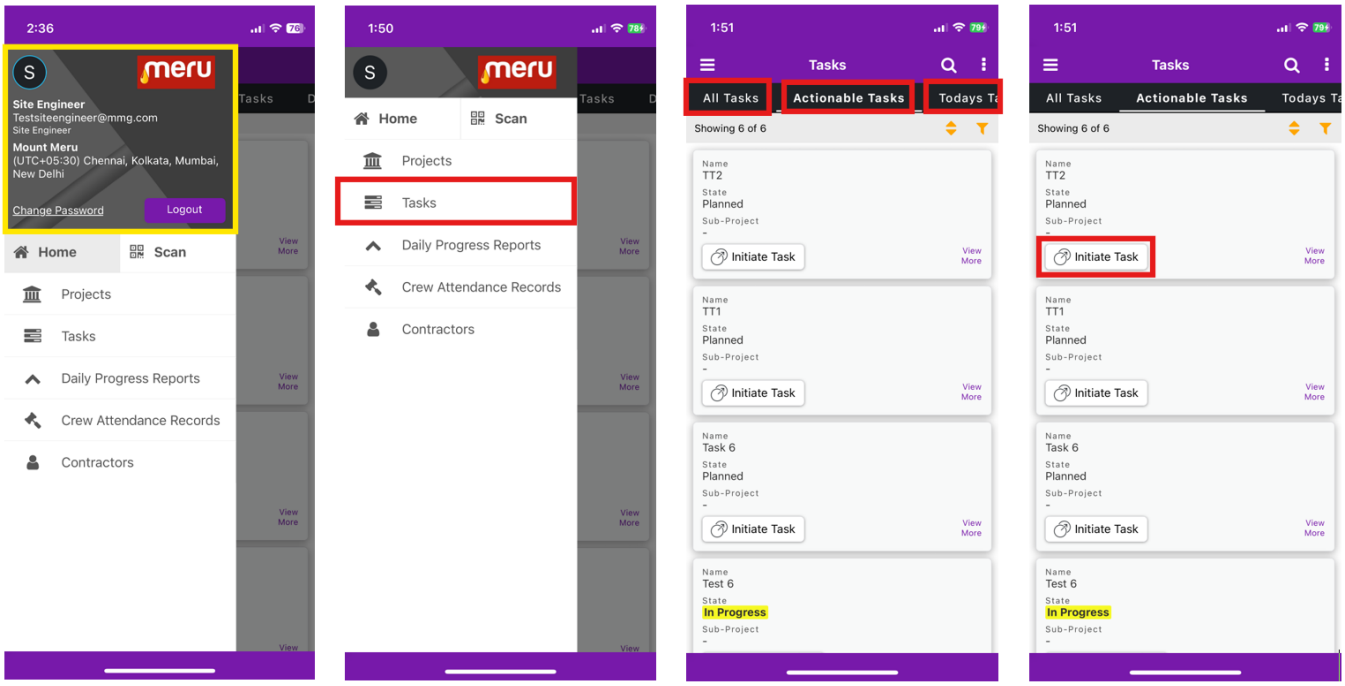

5.3 Updating Work Progress

1. Open the assigned task and click 'Initiate Task' to enable the 'Work Progress' tab. Go to 'Work Progress' tab & click on 'Add Work Progress'

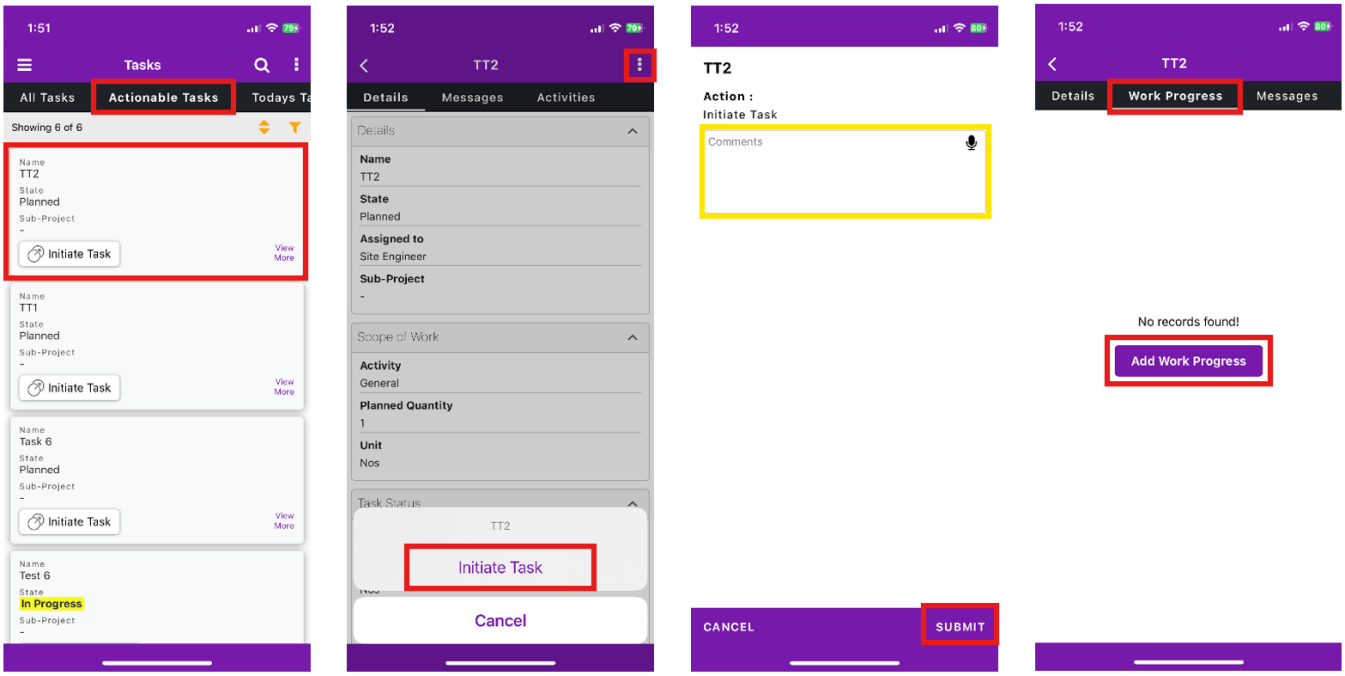

2. Enter all the required work progress details:
   - Actual Completion Date
   - Quantity
   - **Manpower Allocation** (Click '+' to add manpower details)
     1. Contractor

Copyright © All rights reserved

2. Description
3. Planned Labour
4. Type of Engagement
5. Attendance Record

❖ Click ‘Save’

- Photo (Upload or capture in real-time)
- Description
- Document Attachment (Upload relevant files)
- Delay Type (Select from predefined options)
- Delay (in hours)
- Delay Description

3. Click 'Save' to save the updates.

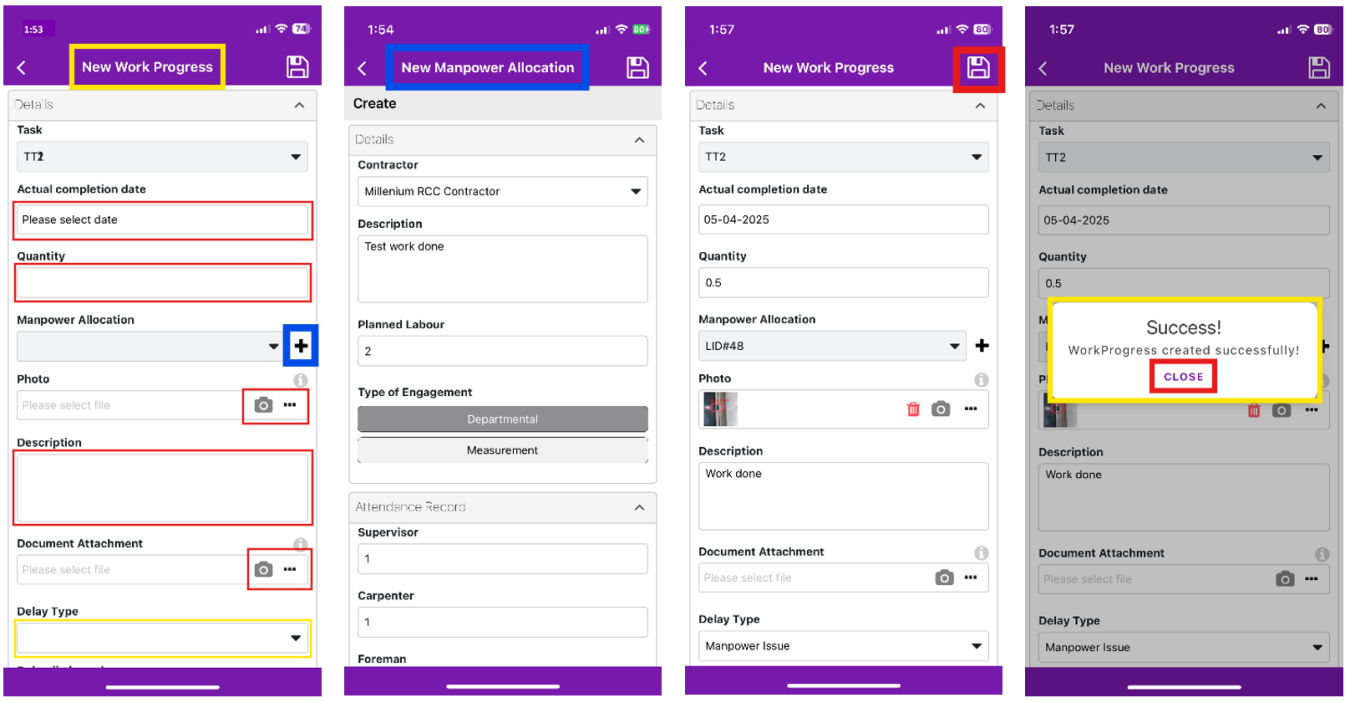

Copyright © All rights reserved

4. If the Task is partially completed, site engineer can add multiple 'work progress' by clicking the '+' button on the right top corner under the 'Work Progress' tab and each instance is recorded.

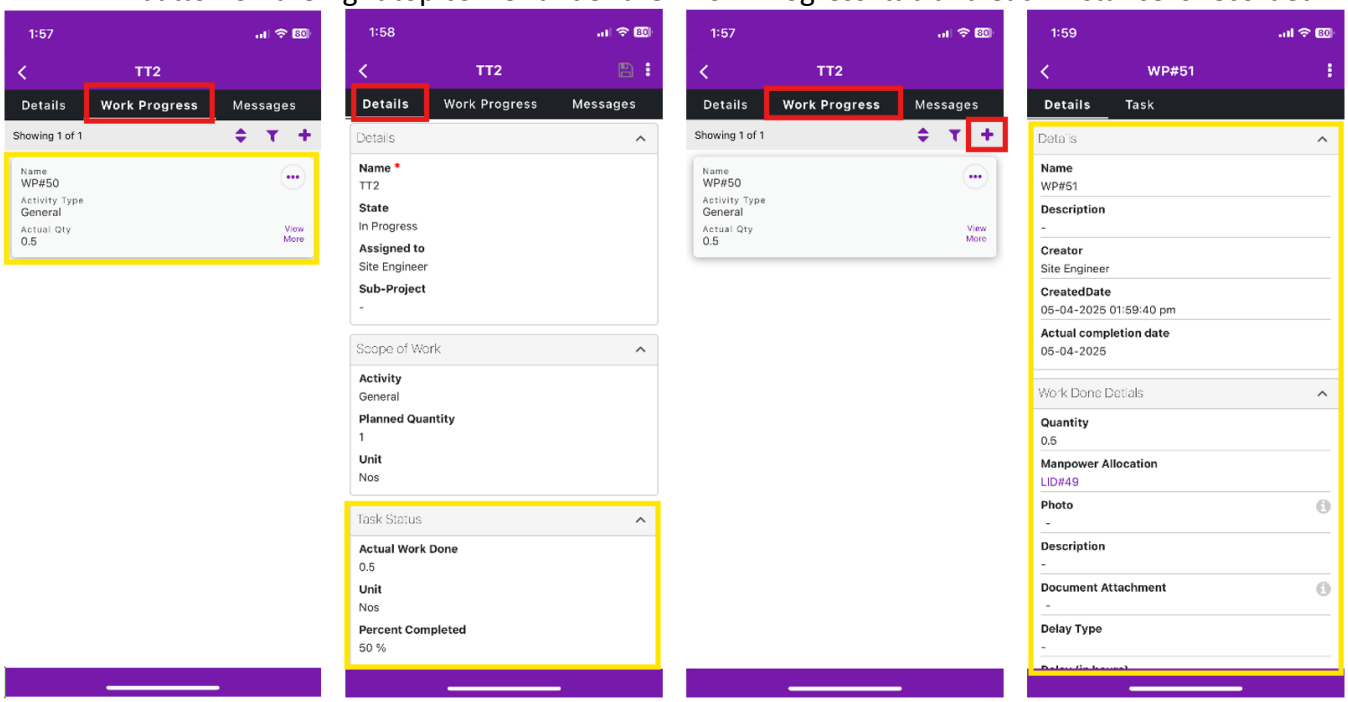

5. Once the Task is completed, use the '3 dots' button to mark the task as completed. Users can go to the 'Work Progress' tab under the task to see the recorded work progress instances.

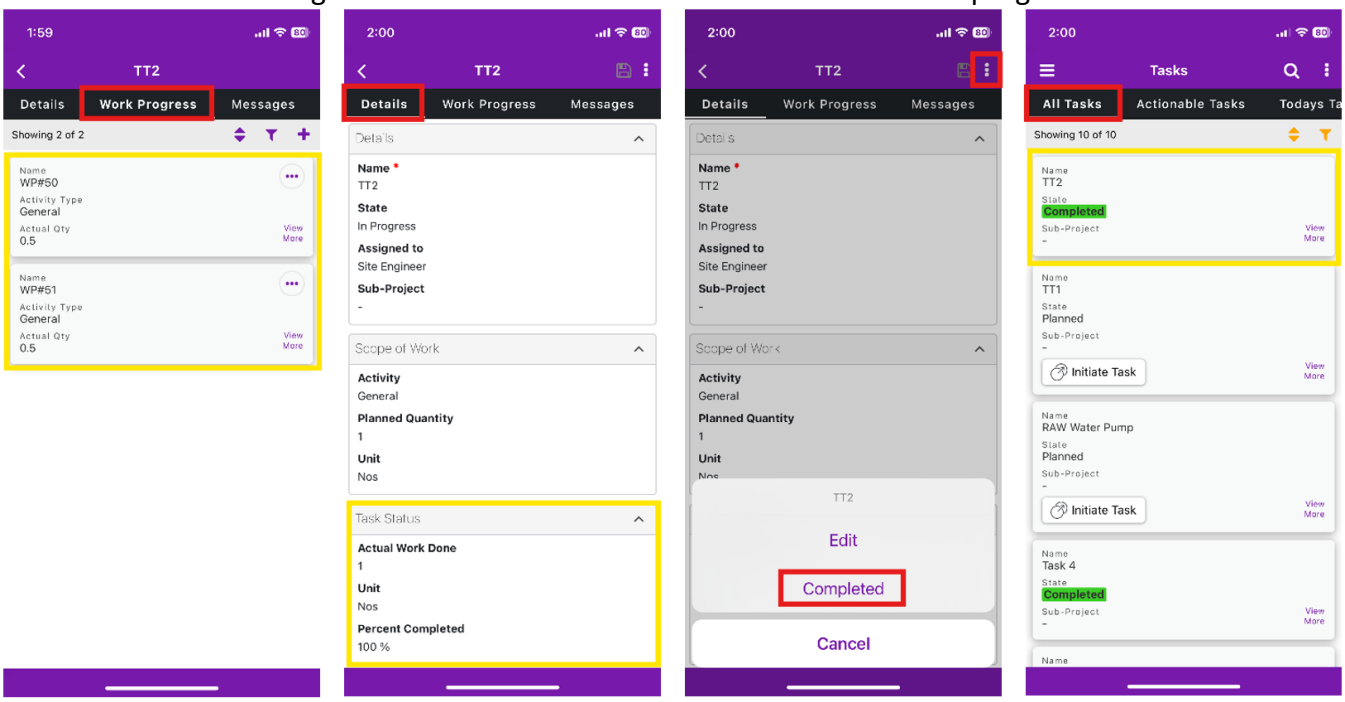

Copyright © All rights reserved

5.4 Task Status View for Project Manager

1. Project Manager can navigate to the 'Details' tab under the particular task and click 'Refresh' to see the updated task status.
2. View the actual work completed and percentage of task completed in real time.

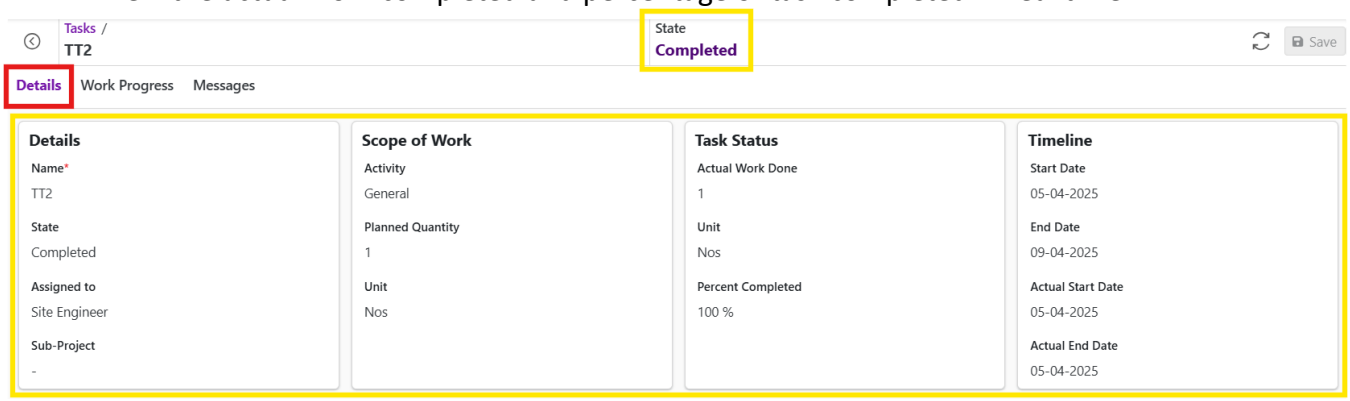

3. Project manager can view the details of the work progress by clicking on the 'Work Progress' tab and can also view the details of each work progress instance by clicking on it.

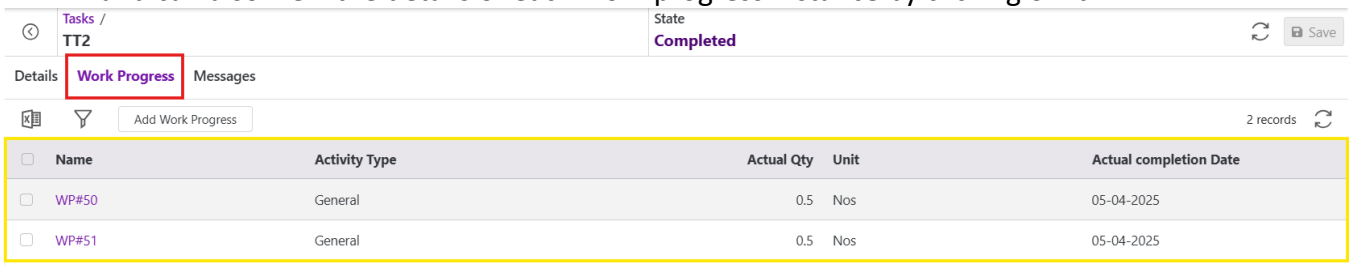

The task updates are auto populated on the Gantt chart, help the project manager to easily track the tasks being completed on the site in real-time.

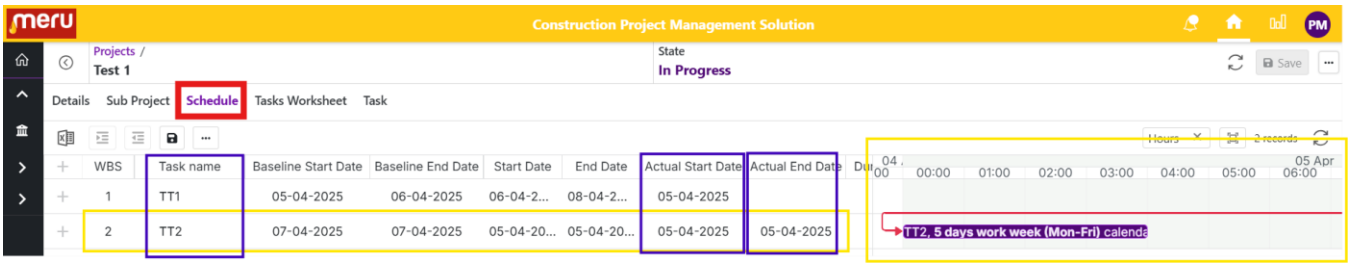

Copyright © All rights reserved

6 Daily Progress Report (DPR)

The Daily Progress Report (DPR) feature helps track day-to-day activities on a project site. These reports are automatically generated every day at 11:00 AM, with one DPR created per project.

1. To Access it, project manager needs to navigate to 'Daily Progress Report' under 'Progress Management' tab click on a particular DPR
2. Under 'Details' tab fill in the 'Location of Work' and select the 'Weather Conditions' and then click on 'Generate DPR'.
3. Click on the generated DPR or click 'DPR Preview' to view the DPR.

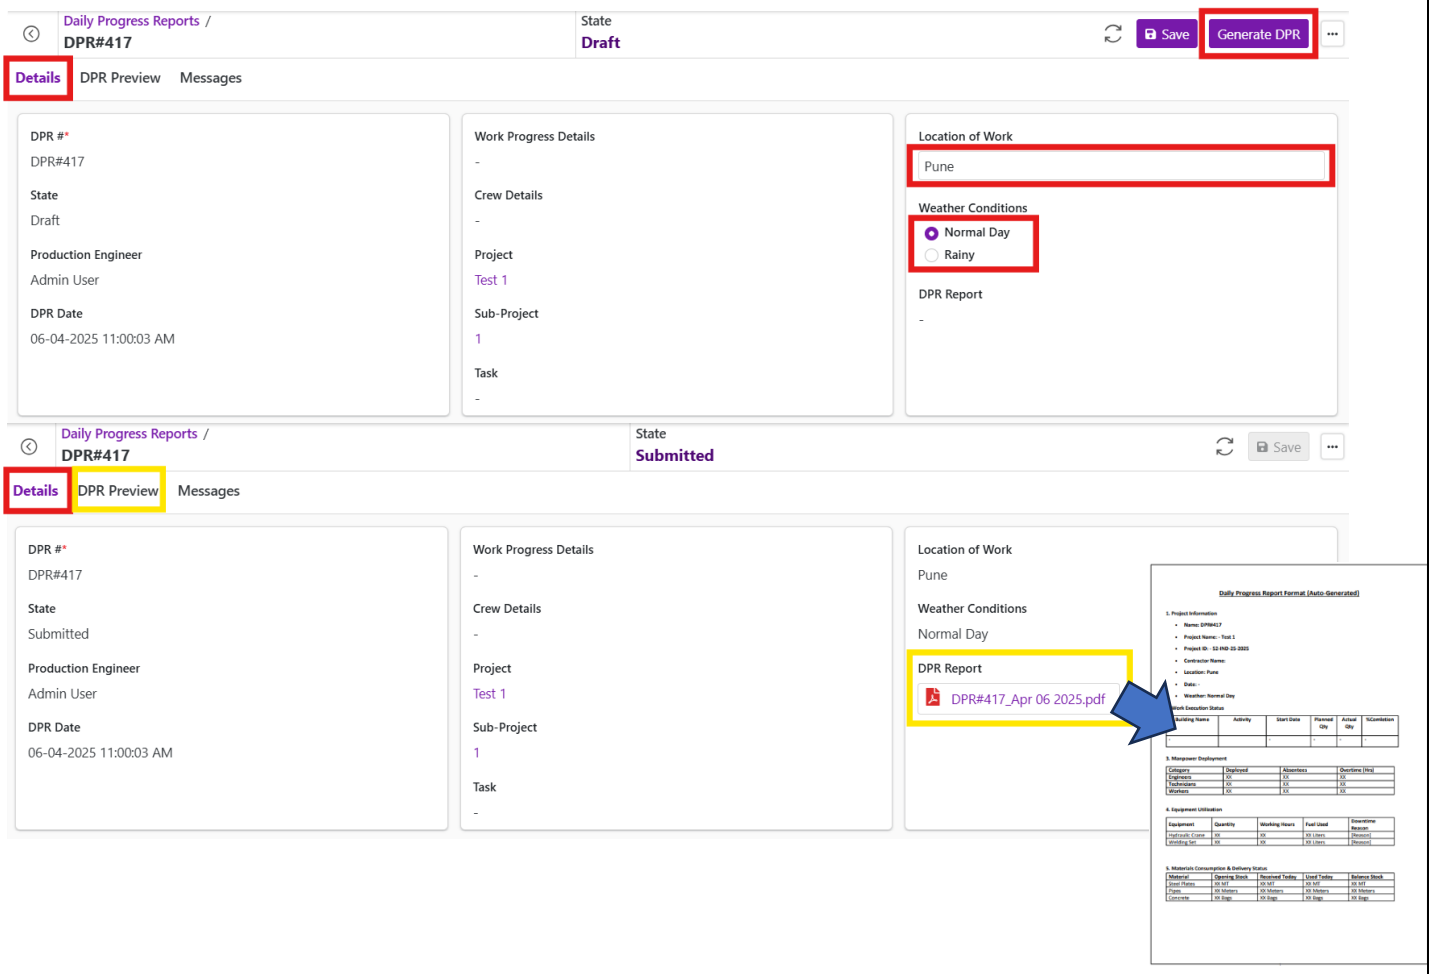

Copyright © All rights reserved

7 Reports

1. Navigate to the Home Tab to view all reports, all configured and generated reports will be listed here.
2. Click to load the latest data and click on any specific report to open it in a new tab for a detailed, enlarged view.

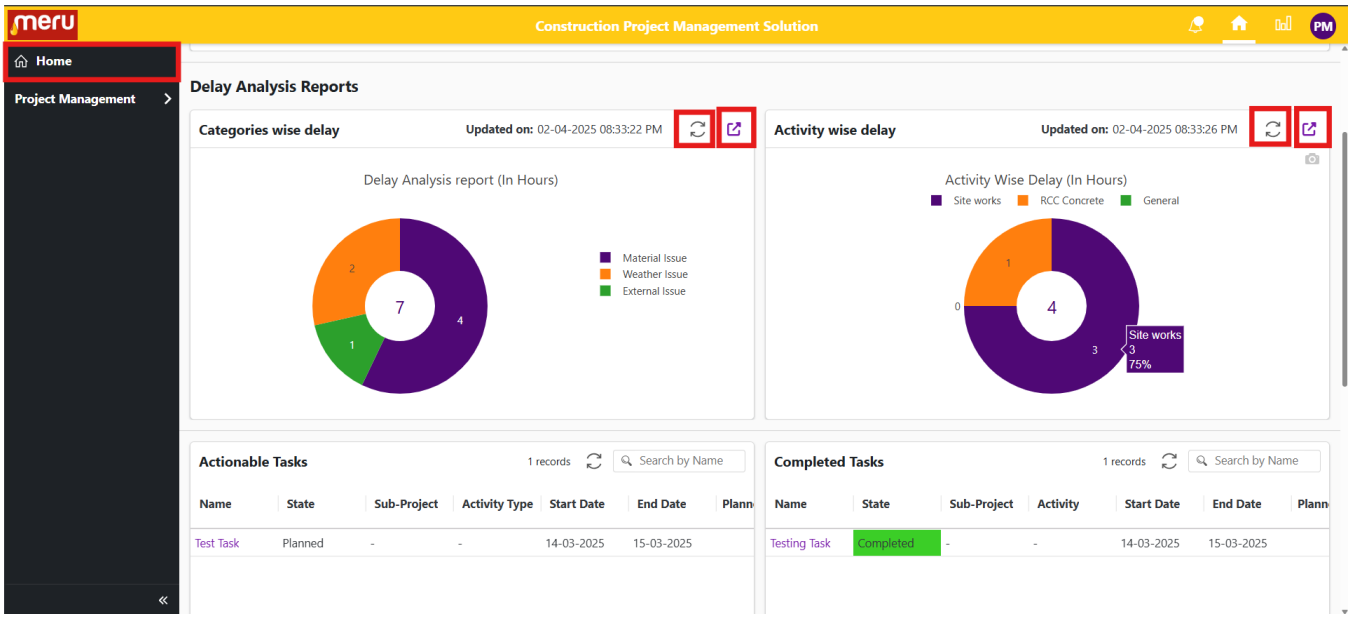

Copyright © All rights reserved
